

Project Schedule



- Updated Project Schedule
 - ▣ Grouped by Project Type and Area
 - ▣ Completed Projects listed in **red**
 - ▣ Schedule Changes
 - Early or late completion can effect all subsequent projects in that Area
 - “Domino Effect”

Project Schedule


Resurfacing

Project Number	Project Description	Project Width	Project Length	Total Cost*	Actual Start	Actual Complete	Target Start	Target Complete
Project Type 01 - Resurfacing								
Area 100								
0206815	Resurface CR 40 from Bridalweath Ln to CR 138 (FY16 Resurfacing - Group 1)	20.00	5.35	\$ 401,012	11/13/2015	1/4/2016	11/14/2015	1/15/2016
0206915	Resurface CR 138 from SR 225 to Bay Minette City Limit (FY16 Resurfacing - Group 1)	20.00	5.15	459,104	11/13/2015	1/4/2016	11/14/2015	1/3/2016
0207115	Resurface E Flying K Rd from SR 59 to CR 49	36.00	0.10	4,250	4/1/2016	7/20/2016	4/1/2016	9/1/2016
0218414	Resurface Mary Hadley Rd from Jack Springs Rd to EOM	20.00	0.52	58,740	9/27/2016	9/30/2016	10/1/2016	12/1/2016
0207016	Resurface CR 112 from US 31 to Phillipsville Rd	24.00	4.10	2,406			2/1/2017	4/1/2017
Area 100 Totals				925,511				
Area 200								
0219014	Resurface CR 48 from 1,900 ft East of SR 181 to CR 33 (FY16 Resurfacing - Group 2)	20.00	1.15	227,592	11/13/2015	2/5/2016	11/14/2015	1/31/2016
0207615	Resurface Lawrence Rd from Lawrence Rd Ext to CR 48 (FY16 Resurfacing - Group 2)	20.00	1.00	76,368	11/13/2015	1/13/2016	11/16/2015	1/15/2016
0207715	Resurface Gunnison Rd from Red Barn Rd to CR 33 (FY16 Resurfacing - Group 2)	18.00	1.01	73,064	11/13/2015	1/13/2016	11/16/2015	1/15/2016
0207815	Resurface Lawrence Rd Ext from Gunnison Rd to Lawrence Rd (FY16 Resurfacing - Group 2)	20.00	0.50	43,849	11/13/2015	1/13/2016	11/16/2015	1/15/2016
0207915	Resurface Red Barn Rd from CR 33 to Gunnison Rd (FY16 Resurfacing - Group 2)	18.00	0.50	40,745	11/13/2015	1/13/2016	11/16/2015	1/15/2016
0207015	Widen and Resurface Flowerwood Rd from SR 59 to EOP	22.00	0.18	5,732	4/1/2016	7/20/2016	4/1/2016	9/1/2016
0207515	Widen and Resurface CR 68 from SR 59 to BBE (FY16 Resurfacing - Group 3)	22.00	4.86	485,429	4/1/2016	7/22/2016	4/1/2016	9/1/2016
0218614	Resurface CR 65 from SR 54 to CR 64 (FY16 Resurfacing - Group 3)	20.00	3.50	231,502	4/1/2016	7/22/2016	4/1/2016	9/1/2016
0218914	Resurface CR 64 from SR 59 to I-10 (FY16 Resurfacing - Group 3)	20.00	8.30	1,672,875	4/1/2016	7/22/2016	4/1/2016	9/1/2016
0219114	Resurface CR 65 from CR 68 to Fox Branch Rd (FY16 Resurfacing - Group 3)	20.00	2.00	144,461	4/1/2016	7/22/2016	4/1/2016	9/1/2016
0207215	Resurface CR 65 from CR 48 to Ketchack Rd (FY16 Resurfacing - Group 3)	20.00	0.50	5,533	4/1/2016	7/22/2016	4/1/2016	9/1/2016
0207315	Resurface Lost River Rd E each direction from end of Lost River Rd (FY16 Resurfacing - Group 4)	18.00	0.86	33,504	6/1/2016	8/1/2016	6/1/2016	8/1/2016
0207415	Widen and Resurface CR 87 from US 90 to Channel 44 Rd (FY16 Resurfacing - Group 4)	22.00	0.15	17,295	6/1/2016	8/1/2016	6/1/2016	8/1/2016
0218514	Resurfacing CR 38 from BBE to CR 87 (FY16 Resurfacing - Group 4)	20.00	3.60	464,681	6/24/2016	9/19/2016	6/1/2016	10/1/2016
Area 200 Totals				3,827,660	6/1/2016	9/19/2016	6/1/2016	10/1/2016
Area 300								
0208415	Widen and Resurface Roscoe Rd from FBE to Cotton Creek Dr (FY16 Resurfacing - Group 2)	24.00	1.60	216,580	11/13/2015	12/10/2015	11/15/2015	12/31/2015
0208015	Resurface CR 49 from CR 16 to Magnolia Springs Town Limit (FY16 Resurfacing - Group 5)	22.00	3.68	286,548	7/20/2016	9/19/2016	6/1/2016	8/31/2016
0208115	Resurface CR 83 from Old Foley Rd to CR 32 (FY16 Resurfacing - Group 5)	24.00	4.54	317,807	6/24/2016	9/19/2016	6/1/2016	10/1/2016
0208315	Resurface Bemis Ln from CR 32 to EOM (FY16 Resurfacing - Group 4)	18.00	0.20	8,170	6/1/2016	8/16/2016	6/1/2016	10/1/2016
0219214	Resurface CR 12 from CR 49 to SR 59 (FY16 Resurfacing - Group 5)	20.00	5.00	390,050	6/1/2016	9/19/2016	6/1/2016	10/1/2016
0219314	Resurface CR 97 from US 98 to Riggs St (FY16 Resurfacing - Group 5)	20.00	3.81	505,486	6/1/2016	8/16/2016	6/1/2016	9/1/2016
0219414	Resurface CR 91 from US 98 to CR 99 (FY16 Resurfacing - Group 5)	20.00	4.10	286,488	6/1/2016	9/19/2016	6/1/2016	10/1/2016
Area 300 Totals				2,011,128				
Totals for Project Type 01 - Resurfacing				71.76 \$ 6,764,300				

*All costs are preliminary, unaudited project costs and include all labor, equipment, material, and contractor costs.



Baldwin County Highway Department
FY 2016 YTD Completed Resurfacing Projects

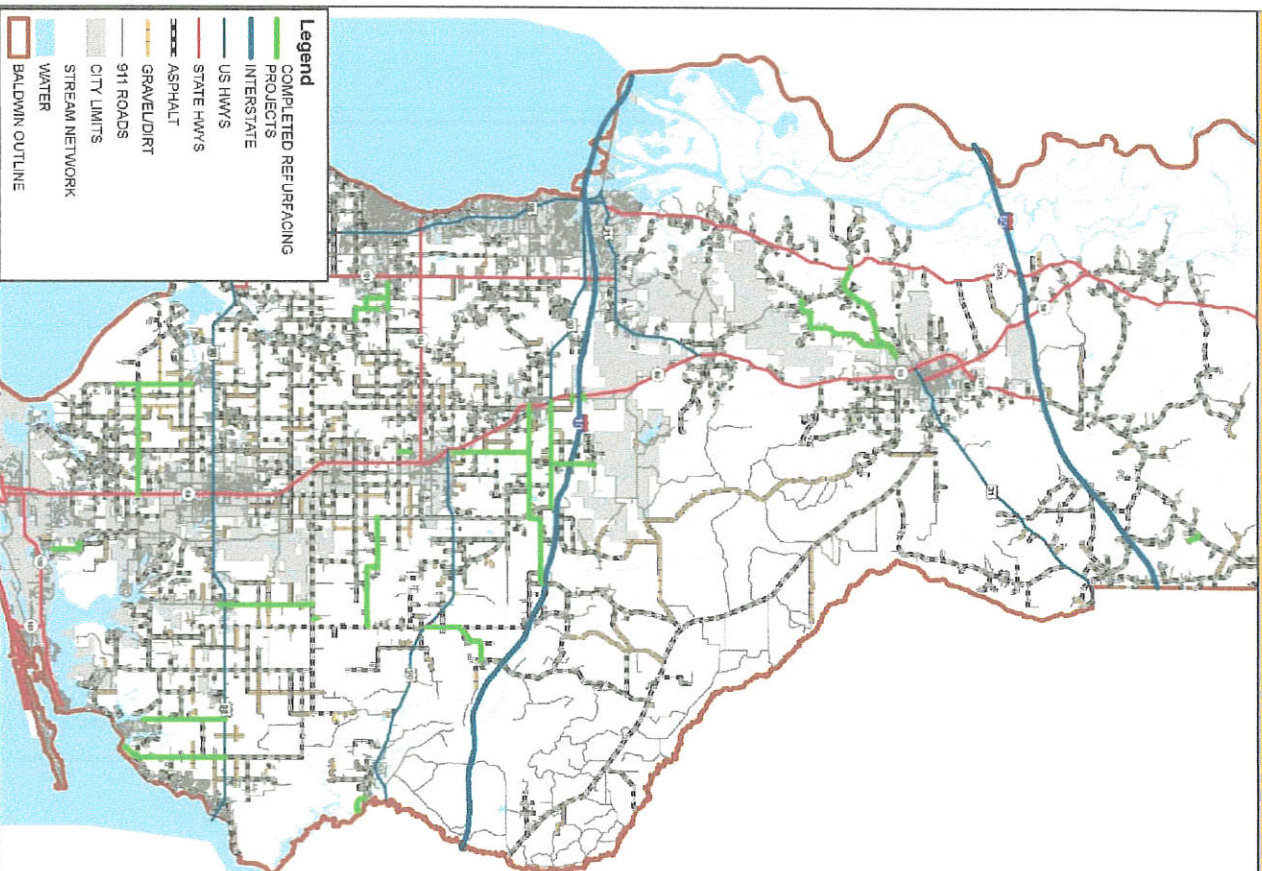

Completed Projects

Resurfacing– Area 200

Project:

0219014 – County Road 48


Resurface County Road 48 from
1,900 ft east of SR 181 to CR 33
(FY 16 Resurfacing – Group 2)

Actual Start Date

11/13/2015

Actual Complete Date

2/5/2016

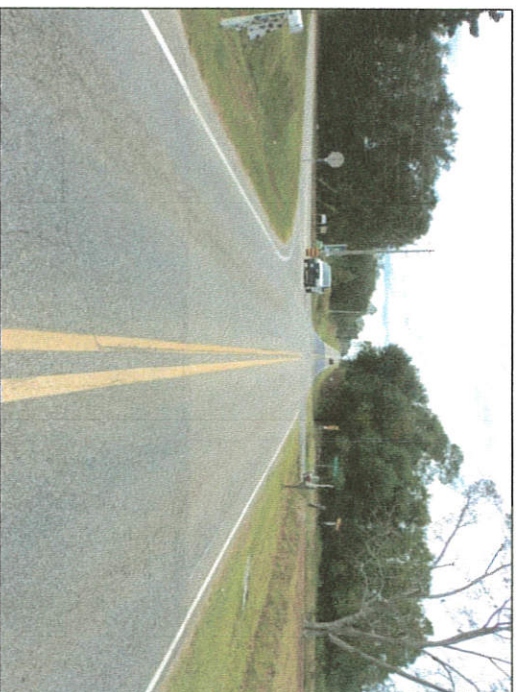

Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207615 – Lawrence Road

Resurface Lawrence Rd from
Lawrence Rd Ext to CR 48
(FY 16 Resurfacing – Group 2)

Actual Start Date

11/13/2015

Actual Complete Date

1/13/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207715 – Gunnison Road


Resurface Gunnison Rd from Red
Barn Rd to CR 33
(FY 16 Resurfacing – Group 2)

Actual Start Date

11/13/2015

Actual Complete Date

1/13/2016

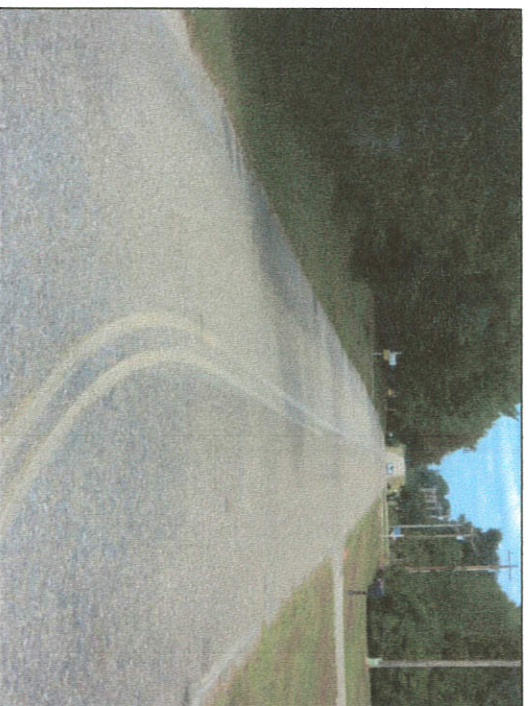

Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207815 – Lawrence Road Ext

Resurface Lawrence Rd Ext from
Gunnison Rd to Lawrence Rd
(FY 16 Resurfacing – Group 2)

Actual Start Date

11/13/2015

Actual Complete Date

1/13/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207915 – Red Barn Road

Resurface Red Barn Rd from CR
33 to Gunnison Rd
(FY 16 Resurfacing – Group 2)

Actual Start Date

11/13/2015

Actual Complete Date

1/13/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207015 – Flowerwood Road

Widen and Resurface Flowerwood Road from State Road 59 to End of Pavement

Actual Start Date

04/01/2016

Actual Complete Date

07/20/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207515 – County Road 68

Widen and Resurface County Road
68 from SR 59 to BBExpress
(FY 16 Resurfacing – Group 3)

Actual Start Date

04/01/2016

Actual Complete Date

07/22/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0218614 – County Road 65

Resurface County Road 65 from
County Road 54 to County Road 64
(FY 16 Resurfacing – Group 3)

Actual Start Date

04/01/2016

Actual Complete Date

07/22/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0218814 – County Road 64

Resurface County Road 64 from
State Road 59 to Interstate 10
(FY 16 Resurfacing – Group 3)

Actual Start Date

04/01/2016

Actual Complete Date

07/22/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0218914 – County Road 65

Resurface County Road 65 from
County Road 68 to Fox Branch Rd
(FY 16 Resurfacing – Group 3)

Actual Start Date


04/01/2016

Actual Complete Date

07/22/2016



Before

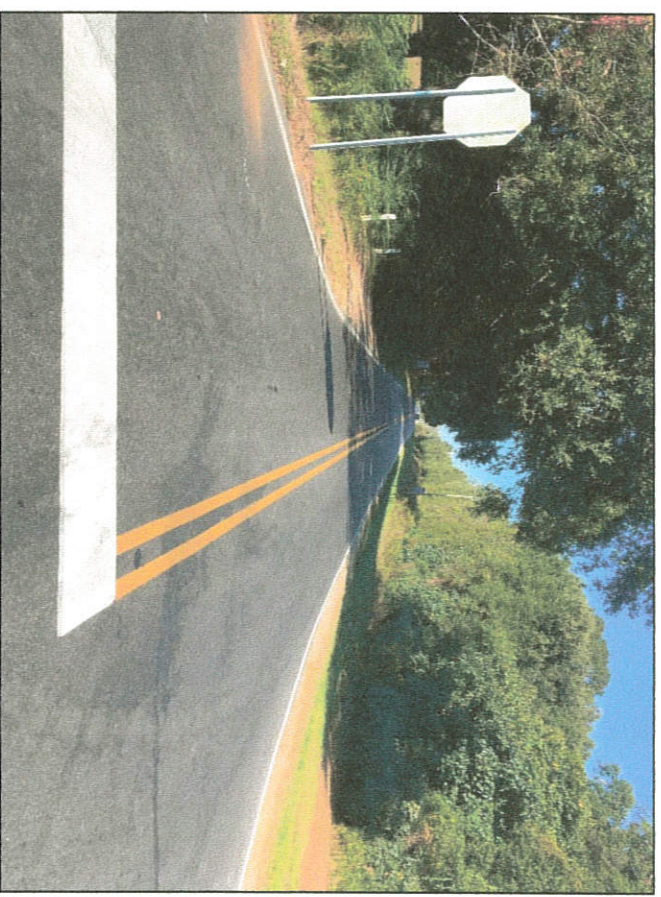

After

Completed Projects

Resurfacing– Area 200

Project:

0219114 – County Road 65

Resurface County Road 65 from
County Road 48 to Krchack Rd
(FY 16 Resurfacing – Group 3)

Actual Start Date

04/01/2016

Actual Complete Date

07/22/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207215 – Lost River Road

Resurface Lost River Rd from River Landing Rd to Lost River Rd E (FY 16 Resurfacing – Group 4)

Actual Start Date

06/01/2016

Actual Complete Date

08/01/2016



Before



After

Completed Projects

Resurfacing– Area 200

Project:

0207315 – Lost River Road East

Resurface Lost River Rd E Each
Direction from End of Lost River Rd
(FY 16 Resurfacing – Group 4)



Before

Actual Start Date

06/01/2016

Actual Complete Date

08/01/2016



After

Completed Projects

Resurfacing– Area 200

Project:

0207415 – County Road 87


Widen and Resurface County Road
87 from US 90 to Channel 44 Rd
(FY 16 Resurfacing – Group 4)

Actual Start Date

06/24/2016

Actual Complete Date

09/19/2016

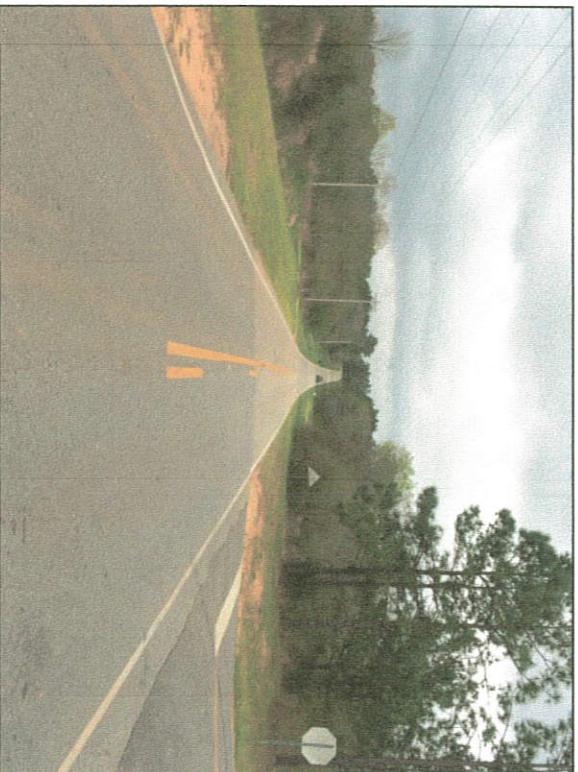

Before



After

Completed Projects

Resurfacing– Area 200

Project:

0218514 – County Road 38


Resurface County Road 38 from
Baldwin Beach Express to CR 87
(FY 16 Resurfacing – Group 4)

Actual Start Date

06/01/2016

Actual Complete Date

09/19/2016

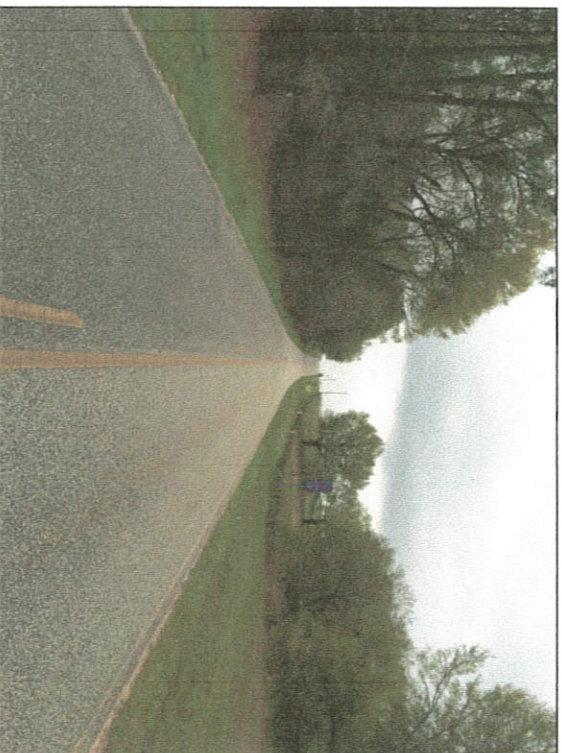

Before



After
