


Project Schedule

Dirt Road Paving

Project Number	Project Description	Project Width	Project Length	Total Cost*	Actual Start	Actual Complete	Target Start	Target Complete
Project Type 03 - Dirt Road Paving								
Area 100								
0216509	G, D, B & Pave Robert White Rd from Hollingsworth Rd to beginning of pavement	20.00	0.55	\$ 229,654	10/1/2014	10/7/2015	8/1/2015	10/7/2015
Area 100 Totals								
			0.55	229,654				
Area 200								
0206311	G, D, B & Pave Grigger Rd from CR 64 east 1.0 miles	20.00	1.00	450,350	5/18/2015	10/12/2015	7/1/2015	12/23/2015
0204114	G, D, B & Pave Newport Rd from EOP to CR 62N	20.00	0.80	389,244	10/1/2015	4/14/2016	10/1/2015	4/14/2016
0203515	G, D, B & Pave Higbee Rd from SR 104 0.75 miles north	22.00	0.75	611,656	1/12/2016	8/31/2016	2/1/2016	7/22/2016
Area 200 Totals								
			2.55	1,451,250				
Area 300								
0205712	G, D, B & Pave Haupt Rd from Bayou Dr to Fish Trap Rd	20.00	0.40	208,363	3/6/2015	12/28/2015	4/1/2015	12/29/2015
0206012	G, D, B & Pave Bayou Dr from Bay Shore Dr to Fish Trap Rd	20.00	0.87	276,598	3/18/2015	12/28/2015	7/1/2015	12/24/2015
0205812	G, D, B & Pave Woerner Rd from CR 87 to CR 95	20.00	2.00	1,608,181	9/23/2015	9/14/2016	10/1/2015	9/12/2016
Area 300 Totals								
			3.27	2,093,143				
Totals for Project Type 03 - Dirt Road Paving								
			6.37	\$ 3,774,047				

*All costs are preliminary, unaudited project costs and include all labor, equipment, material, and contractor costs.

Baldwin County Highway Department
FY 2016 YTD Completed Dirt Road Paving Projects

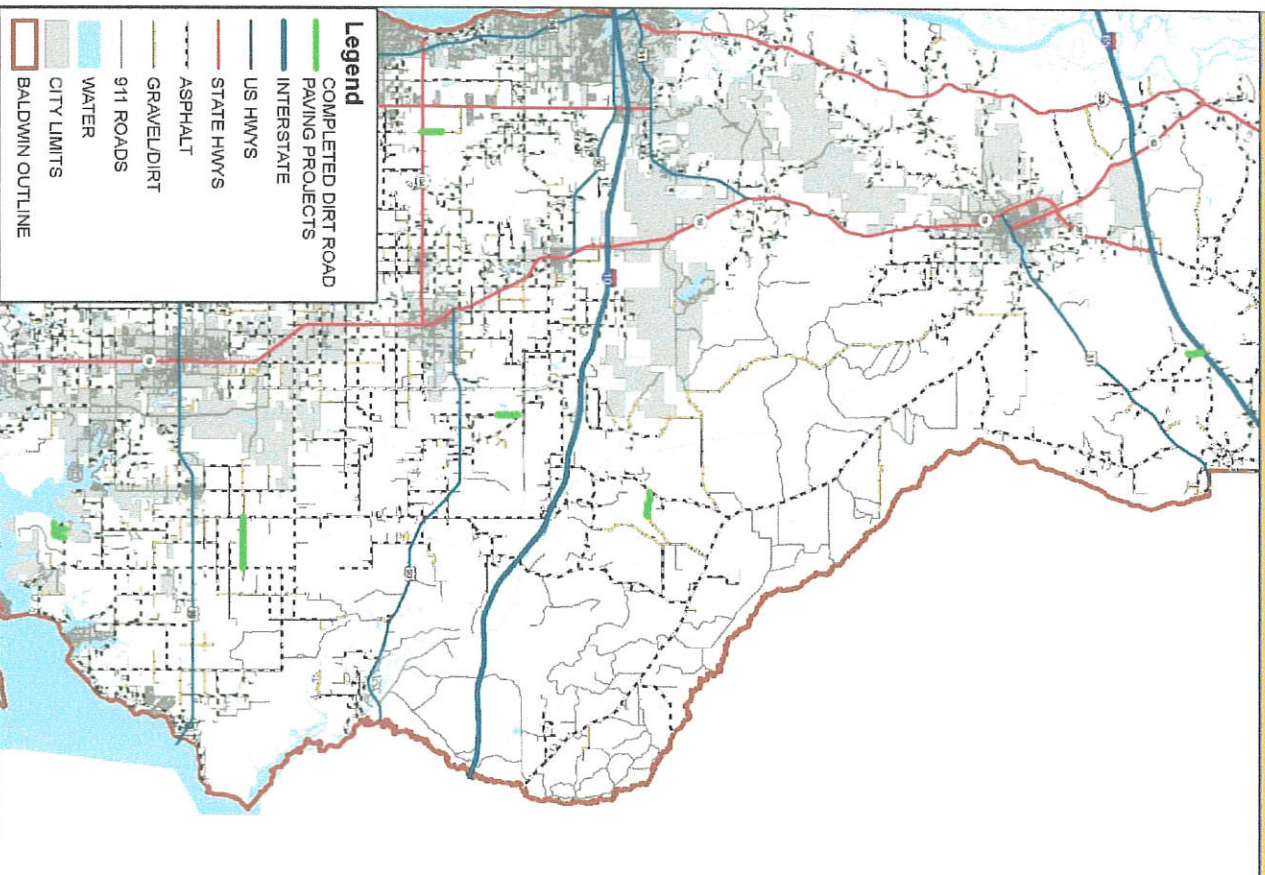

Completed Projects

Dirt Road Paving – Area 200

Project:

0206311 – Grigger Road

G,D,B & Pave Grigger Road from
CR 64 East 1.0 miles

Actual Start Date

05/08/2015

Actual Complete Date

10/12/2015



Before



After

Completed Projects

Dirt Road Paving – Area 200

Project:

0204114 – Newport Road

G, D, B & Pave Newport Rd from
EOP to County Rd 62 N

Actual Start Date Actual Complete Date

10/01/2015

04/14/2016



Before



After

Completed Projects

Dirt Road Paving – Area 200

Project:

0203515 – Higbee Road

G, D, B & Pave Higbee Road from
State Rd 104 0.75 miles North

Actual Start Date

1/12/2016

Actual Complete Date

08/31/2016



Before



After


Project Schedule

New Road Construction / AFMs

Project Number	Project Description	Project Width	Project Length	Project Total Cost*	Actual Start	Actual Complete	Target Start	Target Complete
Project Type 04 - New Road Construction (Contractor)								
Area 100								
Area 100 Totals		-	-	-				
Area 200								
0204815 G, D, B & Pave I-10 Interchange @ CR 68 from CR 64		56.00	1.50	\$ -	3/1/2013	1/11/2016	3/1/2013	4/1/2016
Area 200 Totals		-	-	-				
Area 300								
0209012 G, D, B & Pave Widen CR 20 from SR 59 to S. Hickory St (ATRAP)		36.00	1.00	667,268	1/5/2015	12/11/2015	2/1/2015	12/15/2015
Area 300 Totals		-	-	667,268				
Totals		1.00	\$	667,268				
Project Type 08 - Accept for Maintenance								
Area 100								
Area 100 Totals		-	-	-				
Area 200								
Area 200 Totals		-	-	-				
Area 300								
Area 300 Totals		-	-	-				
Totals for Project Type 08 - Accept For Maintenance		-	-	-				

*All costs are preliminary, unaudited project costs and include all labor, equipment, material, and contractor costs.

Baldwin County Highway Department
FY 2016 YTD Completed New Road Construction
Contractor Projects

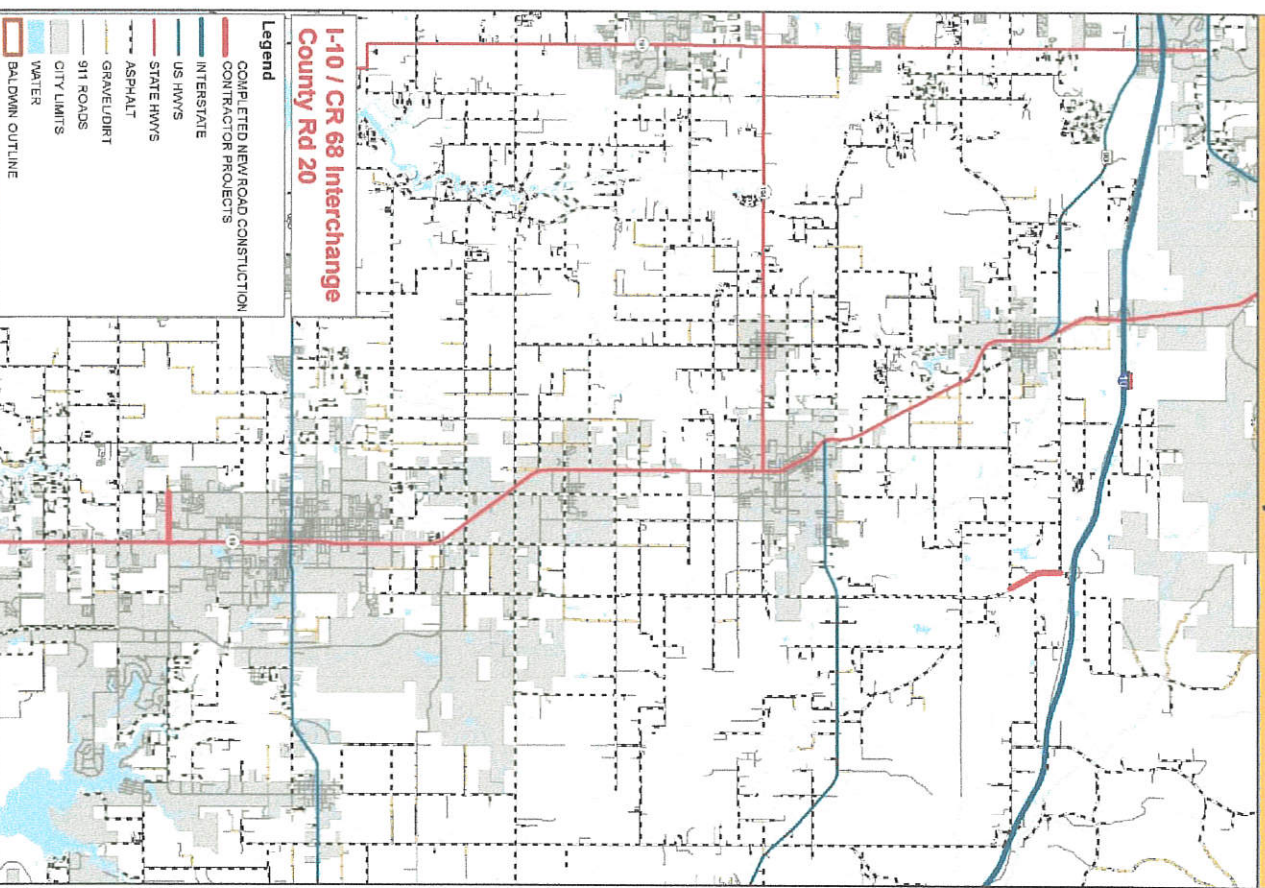

I-10 / CR 68 Interchange
County Rd 20

Legend

- COMPLETED NEW ROAD CONSTRUCTION
- CONTRACTOR PROJECTS
- INTERSTATE
- US HWYS
- STATE HWYS
- ASPHALT
- GRAVEL/DIRT
- 911 ROADS
- CITY LIMITS
- WATER
- BALDWIN OUTLINE

Completed Projects

New Road Construction (Contractor)– Area 200

Project:

0204815 – I-10 Interchange

G, D, B & Pave I-10 Interchange
@ CR 68 from CR 64

Actual Start Date

3/1/2013

Actual Complete Date

1/11/2016



Project Schedule


Bridge Projects

Project Number	Project Description	Project Width	Project Length	Total Cost*	Actual Start	Actual Complete	Target Start	Target Complete
Project Type 11 - Bridge Projects								
Area 100								
Area 100 Totals								
Area 200								
0206412 Bridge Replacement on CR 55 over Branch (FAS)								
Area 200 Totals								
Area 300								
0212809	Bridge culvert & 3 cross drains on CR 32 over Unnamed Creek (FHWA)	-	-	162,340	3/7/2016		3/1/2016	11/1/2016
0215614	Bridge replacement on CR 34 over Negro Creek (ATRIP)	22.00	0.13	310,215	2/29/2016		3/1/2016	4/1/2017
0206113	Bridge Replacement on Keller Rd over Boggy Branch (ATRIP)	22.00	0.06	55,454			2/1/2017	6/1/2017
Area 300 Totals								
Totals for Project Type 11 - Bridge Projects								
Area 100 Totals								
Area 200 Totals								
Area 300 Totals								
Totals for Project Type 11 - Bridge Projects								

*All costs are preliminary, unaudited project costs and include all labor, equipment, material, and contractor costs.



Baldwin County Highway Department
FY 2016 Completed Bridge Projects and Maintained Bridges

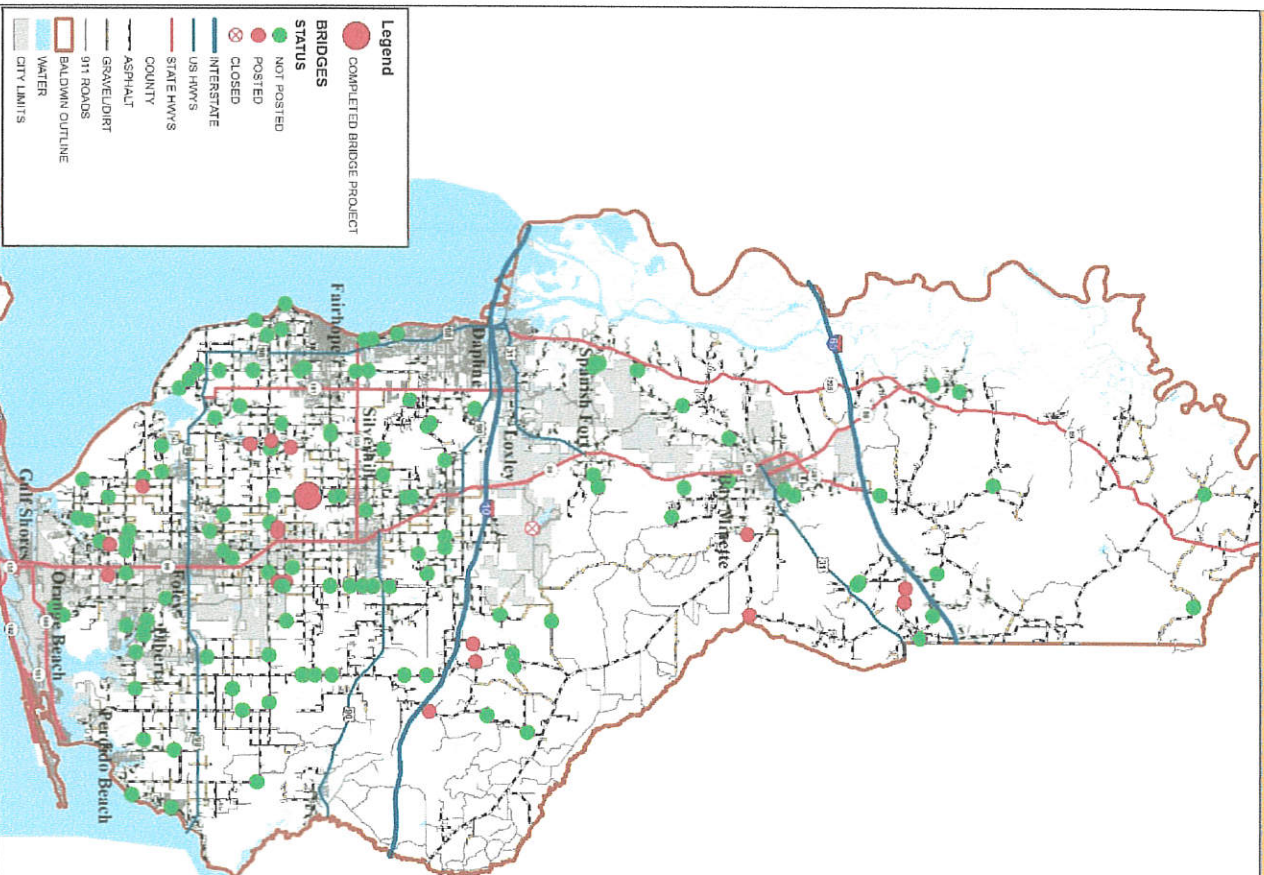

Completed Project

Bridge Project – Area 200

Project:

0206412 – County Road 55

Actual Start Date

02/15/2016

Actual Complete Date

09/23/2016

Bridge Replacement on County Road 55 over Branch (FAS)




Project Schedule

Drainage Improvement

Project Number	Project Description	Project Width	Project Length	Total Cost*	Actual Start	Actual Complete	Target Start	Target Complete
Project Type 18 - Drainage Improvement								
Area 100								
Area 200								
0217114	Drainage Improvements to Sibley St from end of Sibley St to Mobile Bay (EWP)	-	-	279,443	8/25/2015	10/14/2015	9/1/2015	10/14/2015
0217214	Drainage Improvements at end of Boone Ln at end of previous EWP project (EWP)	-	-	287,026	8/26/2015	10/14/2015	9/1/2015	10/14/2015
0207011	Stream Restoration - D'Olive Creek	-	-	\$ 80	7/1/2013	4/18/2016	12/1/2013	8/31/2016
0214814	Drainage Improvements on CR 64 west of CR 65 (FHWA)	-	-	471,362	2/5/2016	4/19/2016	2/1/2016	5/1/2016
0205316	Construct Retention Pond and Ditch adjacent to Lassiter Farm Rd	-	-	130,913	7/21/2016		8/1/2016	10/21/2016
Area 200 Totals				1,168,824				
Area 300								
0206415	Replace Crossdrain on CR 91 north of Maidmont Ln (FEMA) PWH385	-	-	41,325	7/29/2015	10/22/2015	8/15/2015	10/23/2015
0219514	Replace Box Culvert on CR 95 800 ft south of Letterman Rd - Anchor Site (FEMA) PWH293	-	-	290,629	11/18/2015	2/19/2016	11/17/2015	5/1/2016
0203116	Replace crossdrain on Boynton Rd north of Millin Rd (FEMA) PWH310	-	-	45,144	4/11/2016	5/31/2016	4/1/2016	5/27/2016
Area 300 Totals				377,099				
County-wide Projects								
0215514	Drainage Improvements - Hatch Mott MacDonald Emergency Repair Sites (FHWA)	-	-	732,622	8/13/2015	1/26/2016	9/1/2015	1/31/2016
0215814	Drainage Improvements - Volkert Emergency Repair Sites (FHWA)	-	-	755,002	9/9/2015	3/4/2016	9/9/2015	3/5/2016
0217814	Replace crossdrains damaged from the 04/29/14 Rain Event - Preble-Rish Sites (FEMA) PWH264	-	-	987,650	9/15/2015	3/11/2016	10/1/2015	4/20/2016
0217914	Replace crossdrains damaged from the 04/29/14 Rain Event - Jade Sites (FEMA) PWH272	-	-	1,438,107	11/17/2015	4/7/2016	11/18/2015	5/1/2016
0217714	Replace crossdrains damaged from the 04/29/14 Rain Event - GMC Sites (FEMA) PWH309	-	-	1,060,963	1/4/2016	5/6/2016	1/15/2016	5/15/2016
0218114	Replace crossdrains damaged from the 04/29/14 Rain Event - HMR Sites (FEMA) PWH309	-	-	1,095,844	9/23/2015	5/24/2016	10/1/2015	6/1/2016
0215714	Drainage Improvements - KBR Emergency Repair Sites (FHWA)	-	-	1,475,399	2/8/2016	8/30/2016	3/1/2016	9/1/2016
0218014	Replace crossdrains damaged from 04/29/14 Rain Event - Anchor Sites (FEMA) PWH310	-	-	1,489,878	1/14/2016		2/1/2016	8/11/2016
0215914	Drainage Improvements - Thompson Emergency Repair Sites (FHWA)	-	-	615,014	8/8/2016		8/15/2016	4/1/2017
County-wide Project Totals				9,650,479				
Totals for Project Type 18 - Drainage Improvement Projects				\$ 11,196,402				

*All costs are preliminary, unaudited project costs and include all labor, equipment, material, and contractor costs.

Baldwin County Highway Department
FY 2016 Completed Drainage Improvement Projects

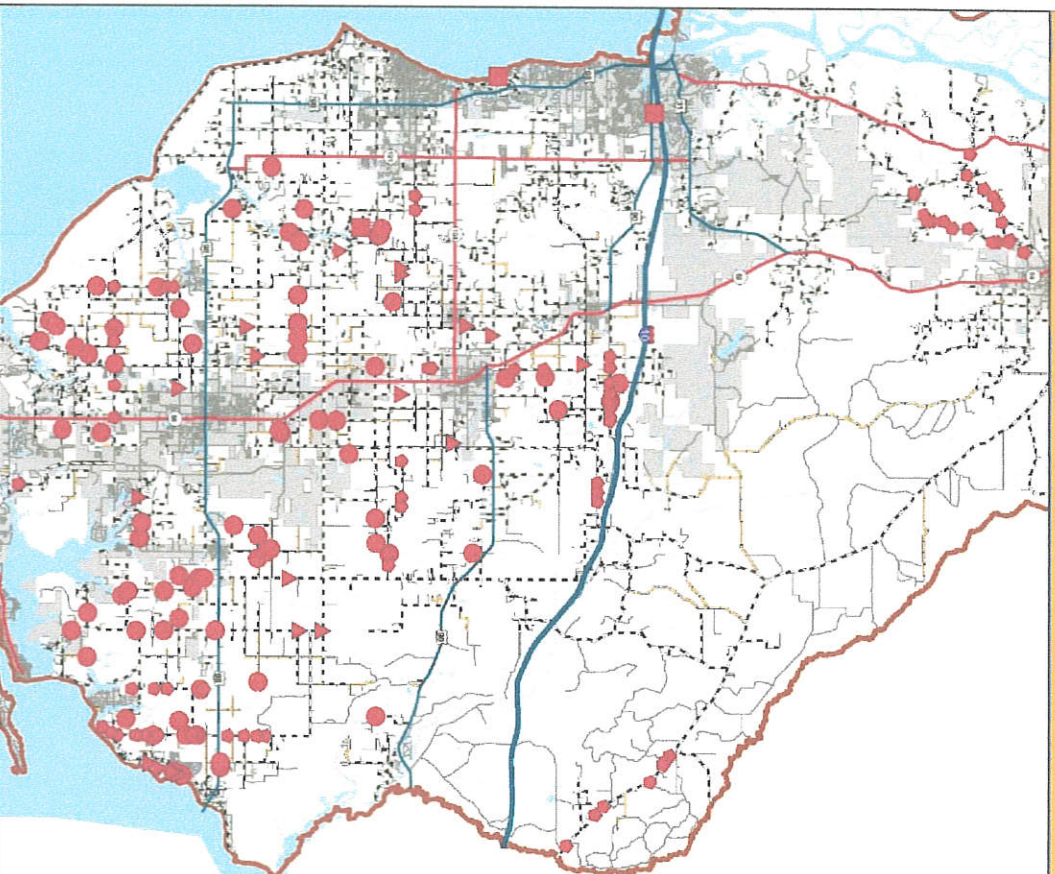

Legend

- COMPLETED FEMA PROJECTS
- ▲ COMPLETED FHWA PROJECTS
- COMPLETED EWP PROJECTS
- ◆ COMPLETED BALDWIN COUNTY PIPE PROJECTS
- INTERSTATE
- US HWYS
- STATE HWYS
- ASPHALT
- GRAVEL/DIRT
- 911 ROADS
- BALDWIN OUTLINE
- WATER
- CITY LIMITS

Completed Projects

Drainage/Flood Reduction– Area 200

Project:

0217214 – Boone Lane

Drainage improvements at end of Boone Lane at end of previous EWP project (EWP)

Actual Start Date

8/26/2015

Actual Complete Date

10/14/2015



Before



After

Completed Projects

Drainage/Flood Reduction– Area 200

Project:

0217114 – Sibley Street

Actual Start Date

8/25/2015

Actual Complete Date

10/14/2015

Drainage improvements on Sibley St from End of Sibley St to Mobile Bay (EWP)



Before



After

Completed Projects

Drainage/Flood Reduction– Area 200

Project:

0214814 – County Road 64

Drainage Improvements on
County Road 64 west of County
Road 65 (FHWA)

Actual Start Date

2/5/2016

Actual Complete Date

4/19/2016



Before



After

In Progress Projects

Drainage/Flood Reduction– Area 200

Project:

0205316 – Lassiter Farm Road

Construct Retention Pond and
Ditch adjacent to Lassiter Farm
Road


Actual Start Date

07/21/2016

Actual Complete Date



Before

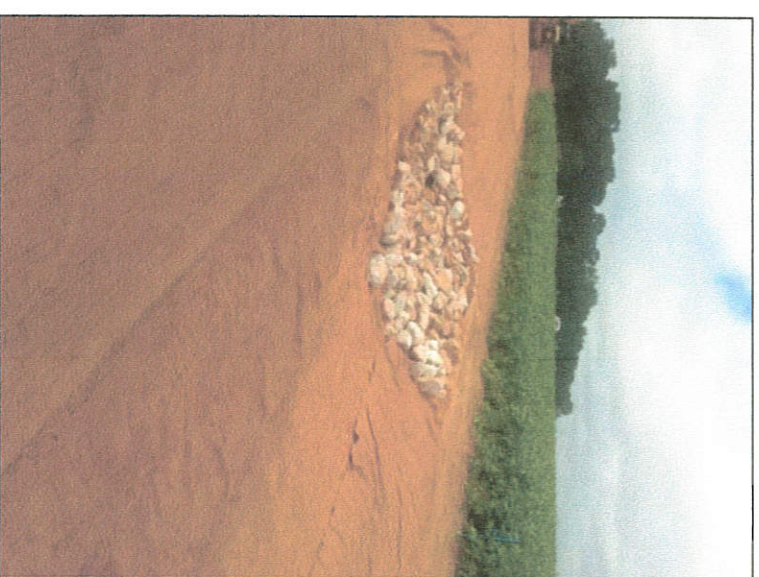

During
